

Construction Update


June 13, 2024



Stage I Area Update:

Over the last two weeks, the contractor adjusted the drainage structures on Driftwood Court, completed the 30-inch storm sewer installation and paved the multi-use path alongside Stonegate Road and Wynnfield Drive. The contractor also adjusted drainage structures with new ADA frames and grates at various locations to enhance accessibility throughout the Stage I area.

Over the next few weeks, the contractor will complete the installation of storm sewer and drainage structures at Cloverdale Lane and Arbordale Court. Fun fact, RCP has a lifespan of 50-75 years and is highly durable, allowing rainfall runoff to drain away from properties safely. The contractor will also begin milling the existing asphalt pavement starting Thursday, 6/13 through Tuesday, 6/18 and complete base stabilization which includes mixing cement with the existing stone base creating a more durable road base to extend the life of the road. This work is expected to begin on Monday, 6/17 and continue for 3-4 days with the Stage I portion of the project.

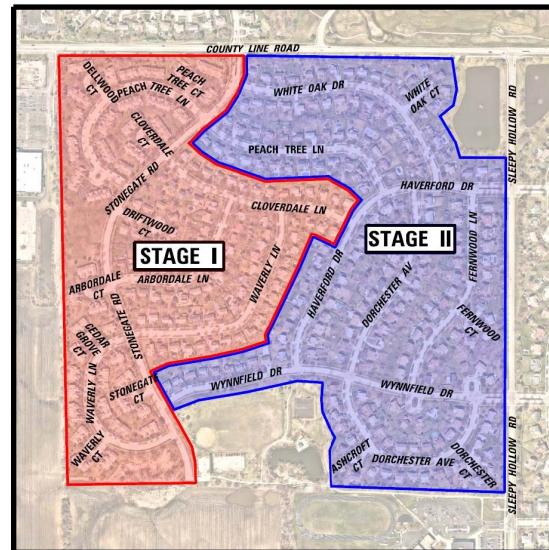

RCP pipe installation

Stage II Area Update:

In the Stage II area of the project, the contractor continued drainage structure adjustments, as well as framing and pouring curb and gutter, sidewalk, and driveway aprons at various locations on Haverford Drive,

White Oak Drive, Peach Tree Lane and Dorchester Avenue. Root pruning also took place at various locations.

Upcoming work for this area includes continuing the removals, framing, and pouring the new concrete for curb and gutter, sidewalk, and driveway aprons at various locations on Dorchester Avenue, Fernwood Court and Wynnfield Drive.



Driveway apron pouring in Stage II

Questions or concerns?

Raz Calin

RCalin@cbbel.com

willoughbyfarmsrehabproject.org



Metro Strategies Group, LLC. | 1901 Butterfield Road Suite 260 | Downers Grove, IL 60515
US

[Unsubscribe](#) | [Update Profile](#) | [Constant Contact Data Notice](#)



Try email marketing for free today!
