

Construction Update

May 29, 2024



Stage I Area Update:


Over the last two weeks, the contractor completed the drainage improvement work at the intersection of Cloverdale and Waverly lanes. The contractor also installed the storm manhole at Cloverdale and Arbordale lanes, poured curb and gutter and sidewalk gaps, and filled potholes at various locations.

Over the next few weeks, the contractor will install the new reinforced concrete pipe (RCP) storm sewer on Cloverdale Lane. RCP is highly durable, with a lifespan of 50-75 years, and allows rainfall runoff to drain away from properties safely. The contractor will also begin storm sewer work at the Cloverdale and Arbordale lanes intersection and complete HMA driveways.

Stage II Area Update:

In the Stage II area of the project, the contractor performed concrete saw cuts, began removals and started framing and pouring sidewalks, curb and gutter at various locations on Haverford Drive, White Oak Drive, White Oak Court, and Peach Tree Lane.

Planned work for this area includes continuing the saw cuts, removals, framing, and pouring the new concrete for curb and gutter, sidewalk and driveway aprons at various locations on White Oak Drive, Haverford Drive, Dorchester Avenue,

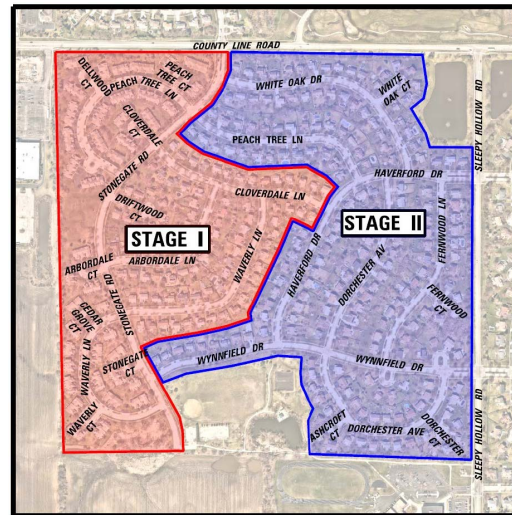

Sidewalk and curb concrete pour



8 ft. diameter manhole at Cloverdale

and Peach Tree Lane. The multi-use path will also be constructed adjacent to Willoughby Farms Park on Stonegate Road and Wynnfield Drive.

and Arbordale lanes

Questions or concerns?

Raz Calin

RCalin@cbbel.com

willoughbyfarmsrehabproject.org



Metro Strategies Group, LLC. | 1901 Butterfield Road Suite 260 | Downers Grove, IL 60515
US

[Unsubscribe](#) | [Update Profile](#) | [Constant Contact Data Notice](#)



Try email marketing for free today!
